

Plan of Action and Milestones (POA&M)

Orion Citizen Services Platform (OCSP)

Organization: Orion Government Solutions
System ID: OCSP-001
Document Version: 1.0
Document Status: Draft for Review
System Owner: Director of Government Platforms
Prepared By: Junior GRC Analyst
Source Assessment Report: SAR-OCSP-2026-07
Assessment Period: July–August 2026
Date: August 2026

Document Control

Version	Date	Author	Description	Status
1.0	August 2026	Junior GRC Analyst	Initial POA&M based on SAR findings	Draft

Approval and Review

Role	Name	Status
System Owner	Director of Government Platforms	Pending
Information System Security Officer	Assigned Security Officer	Pending
Chief Information Security Officer	CISO	Pending
Authorizing Official	Designated Authorizing Official	Pending

1. Purpose

The purpose of this Plan of Action and Milestones is to document and track the remediation of security weaknesses identified during the security assessment of the Orion Citizen Services Platform.

This POA&M provides a structured method for:

- Tracking identified weaknesses;

- Assigning remediation ownership;
- Defining corrective actions;
- Establishing milestones;
- Setting target completion dates;
- Monitoring remediation progress;
- Documenting completion evidence; and
- Supporting reassessment and finding closure.

This POA&M is directly linked to the Security Assessment Report for the Orion Citizen Services Platform.

2. Source Assessment

The weaknesses documented in this POA&M were identified during the assessment documented in:

SAR-OCSP-2026-07

The assessment identified four findings requiring remediation.

3. POA&M Status Summary

POA&M ID	Related Finding	Control	Priority	Owner	Status
POAM-001	SAR-OCSP-001	AC-2	High	IAM Team	Open
POAM-002	SAR-OCSP-002	CM-2	Medium	Infrastructure Engineering	Open
POAM-003	SAR-OCSP-003	IR-3	Medium	Security Operations	Open
POAM-004	SAR-OCSP-004	SR-3	Medium	Vendor Risk Management	Open

4. POA&M Status Definitions

Status	Definition
Open	Weakness has been identified and remediation has not yet been completed
In Progress	Remediation activities are actively underway
Pending Validation	Remediation has been reported as complete and requires validation
Closed	Remediation has been validated and the finding has been formally closed
Risk Accepted	The responsible authority has formally accepted the associated risk

Status	Definition
Delayed	Remediation is not progressing according to the approved schedule

5. POA&M Entry — POAM-001

Account Lifecycle Management

Finding Reference

SAR-OCSP-001

Control

AC-2 — Account Management

Priority

High

Finding Title

Inactive accounts were not consistently disabled within the defined organizational timeframe.

Weakness Description

Review of account management records identified instances where inactive user accounts remained enabled beyond the organization's defined account lifecycle requirements.

The account management process relied partially on manual review and did not consistently ensure timely identification and disabling of inactive accounts.

Risk

Active accounts that are no longer required may provide unnecessary opportunities for unauthorized access.

If credentials associated with an unnecessary account are compromised, an attacker may use the account to access system resources.

Affected System

Orion Citizen Services Platform
OCSP-001

Responsible Organization

Identity and Access Management Team

Remediation Strategy

Orion Government Solutions will strengthen account lifecycle management by implementing a consistent process for identifying, reviewing, disabling, and documenting inactive accounts.

Where practical, the organization will use automated identity management capabilities to reduce reliance on manual processes.

Remediation Milestones

Milestone	Description	Owner	Target Date	Status
M1	Define inactive account criteria	IAM Team	August 2026	Open
M2	Identify current inactive accounts	IAM Team	August 2026	Open
M3	Implement automated or monitored detection	IAM Team	September 2026	Open
M4	Establish disablement workflow	IAM Team	September 2026	Open
M5	Perform validation review	Security / GRC	September 2026	Open

Planned Completion Date

September 30, 2026

Completion Evidence

Expected evidence includes:

- Updated account lifecycle procedure
 - Inactive account report
 - Account disablement records
 - Updated identity management configuration
 - Validation review
-

Closure Criteria

This POA&M item may be closed when:

- Inactive account criteria are documented;
 - The account lifecycle process is implemented;
 - Inactive accounts are consistently identified and disabled;
 - Evidence demonstrates the process is operating;
 - The control is reassessed; and
 - The assessor determines the weakness has been remediated.
-

Current Status

Open

6. POA&M Entry — POAM-002

Configuration Baseline Management

Finding Reference

SAR-OCSP-002

Control

CM-2 — Baseline Configuration

Priority

Medium

Finding Title

Configuration baseline documentation was incomplete for selected system components.

Weakness Description

Configuration baseline documentation was not consistently maintained for all applicable system components within the assessment scope.

Although technical configuration standards existed for selected components, baseline documentation was incomplete or not consistently linked to relevant system components.

Risk

Incomplete configuration baselines may make it difficult to:

- Identify unauthorized changes;
 - Detect configuration drift;
 - Maintain consistent security settings;
 - Validate system security posture.
-

Affected System

Orion Citizen Services Platform
OCSP-001

Responsible Organization

Infrastructure and Platform Engineering

Remediation Strategy

Orion Government Solutions will establish and maintain complete configuration baselines for applicable OCSF components.

Each applicable component will have an approved configuration baseline, designated owner, review frequency, and documented change process.

Remediation Milestones

Milestone	Description	Owner	Target Date	Status
M1	Identify components requiring baselines	Infrastructure Engineering	August 2026	Open
M2	Document approved configurations	Infrastructure Engineering	September 2026	Open
M3	Assign baseline ownership	Infrastructure Manager	September 2026	Open
M4	Establish baseline review schedule	Infrastructure Manager	September 2026	Open
M5	Perform configuration validation	Security / Infrastructure	October 2026	Open

Planned Completion Date

October 15, 2026

Completion Evidence

Expected evidence includes:

- Approved configuration baseline documentation
 - Component inventory
 - Configuration ownership records
 - Baseline review schedule
 - Configuration validation report
-

Closure Criteria

This POA&M item may be closed when:

- Applicable components are identified;

- Approved configuration baselines are documented;
 - Baseline ownership is assigned;
 - A review process is established;
 - Configuration validation is performed; and
 - The control is reassessed.
-

Current Status

Open

7. POA&M Entry — POAM-003

Incident Response Exercise

Finding Reference

SAR-OCSP-003

Control

IR-3 — Incident Response Testing

Priority

Medium

Finding Title

Evidence of a recent incident response exercise was not available.

Weakness Description

The organization maintained incident response procedures; however, evidence of a recent exercise validating the effectiveness of those procedures was outdated.

The assessment team could not verify that relevant personnel had recently participated in an exercise designed to validate incident response coordination and escalation procedures.

Risk

Without regular incident response exercises, weaknesses in communication, escalation, roles, responsibilities, and coordination may remain unidentified.

Affected System

Orion Citizen Services Platform
OCSP-001

Responsible Organization

Security Operations and Incident Response Team

Remediation Strategy

Orion Government Solutions will conduct and document a current incident response exercise involving relevant technical, security, business, and management stakeholders.

The exercise will test the organization's ability to coordinate and respond to a realistic security incident scenario.

Remediation Milestones

Milestone	Description	Owner	Target Date	Status
M1	Define exercise scenario	Incident Response Team	August 2026	Open
M2	Identify participants	Security Operations	August 2026	Open
M3	Conduct tabletop exercise	Security Operations	August 2026	Open
M4	Document observations and weaknesses	Incident Response Team	August 2026	Open
M5	Track improvement actions	GRC / Security Operations	September 2026	Open

Planned Completion Date

August 31, 2026

Completion Evidence

Expected evidence includes:

- Approved exercise scenario
 - Participant list
 - Exercise agenda
 - Exercise report
 - Lessons learned
 - Improvement action tracker
-

Closure Criteria

This POA&M item may be closed when:

- A current incident response exercise is completed;
 - Relevant stakeholders participate;
 - Results are documented;
 - Identified improvement actions are tracked; and
 - Evidence is reviewed and accepted by the responsible security authority.
-

Current Status

Open

8. POA&M Entry — POAM-004

Critical Vendor Security Reassessment

Finding Reference

SAR-OCSP-004

Control

SR-3 — Supply Chain Controls and Processes

Priority

Medium

Finding Title

Security reassessment of a critical third-party vendor was not completed according to the defined review schedule.

Weakness Description

A critical third-party service provider had not completed its scheduled security reassessment within the required review period.

The vendor remained an active dependency for system operations.

Risk

Delayed reassessment of critical vendors may result in an outdated understanding of:

- Vendor security posture;
- Control effectiveness;
- New vulnerabilities;
- Changes to vendor services;
- Changes to the vendor's risk profile.

Affected System

Orion Citizen Services Platform
OCSP-001

Responsible Organization

Remediation Strategy

Orion Government Solutions will complete the overdue reassessment of the critical vendor and improve the process for tracking future vendor review deadlines.

The organization will establish appropriate escalation procedures for overdue assessments.

Remediation Milestones

Milestone	Description	Owner	Target Date	Status
M1	Confirm critical vendor classification	Vendor Risk Team	August 2026	Open
M2	Request updated vendor security evidence	Vendor Risk Team	August 2026	Open
M3	Complete vendor reassessment	Vendor Risk Team	September 2026	Open
M4	Document reassessment results	Vendor Risk Team	September 2026	Open
M5	Implement deadline tracking and escalation	Vendor Risk Team	October 2026	Open

Planned Completion Date

October 15, 2026

Completion Evidence

Expected evidence includes:

- Updated vendor security assessment
- Vendor security documentation
- Completed security questionnaire
- Updated vendor risk rating
- Review approval
- Vendor reassessment tracking record

Closure Criteria

This POA&M item may be closed when:


- The critical vendor reassessment is completed;
- Current security evidence is reviewed;
- The vendor risk assessment is updated;
- Future review deadlines are tracked;
- Any additional vendor weaknesses are documented; and
- The control is reassessed where required.

Current Status

Open

9. Remediation Timeline

```
July 2026
|
+-- Security assessment completed
|
v
August 2026
|
+-- Incident response exercise
+-- Account lifecycle criteria defined
+-- Configuration baseline inventory
+-- Vendor reassessment initiated
|
v
September 2026
|
+-- Account lifecycle remediation
+-- Incident response improvements
+-- Vendor reassessment completion
|
v
October 2026
|
+-- Configuration baseline validation
+-- Vendor deadline tracking improvements
|
v
```



10. POA&M Tracking Dashboard

POA&M ID	Finding	Priority	Current Status	Target Date
POAM-001	Account Lifecycle Management	High	Open	September 30, 2026
POAM-002	Configuration Baseline Management	Medium	Open	October 15, 2026
POAM-003	Incident Response Exercise	Medium	Open	August 31, 2026
POAM-004	Vendor Security Reassessment	Medium	Open	October 15, 2026

11. Remediation Progress Tracking

POA&M status must be reviewed periodically.

Progress reviews should consider:

- Milestones completed;
- Milestones delayed;
- New risks;
- Changes to remediation plans;
- Resource requirements;
- Updated target dates;
- Validation requirements.

Any significant delay should be documented and escalated to appropriate stakeholders.

12. Risk Acceptance

If a weakness cannot be remediated within the planned timeframe, the responsible organization must evaluate whether formal risk acceptance is appropriate.

Risk acceptance must:

- Be formally documented;
- Identify the specific weakness;
- Identify the associated risk;
- Identify compensating controls where applicable;
- Define an expiration or review date;
- Be approved by the appropriate risk authority.

A POA&M item must not be marked closed solely because remediation is delayed.

13. Remediation Validation

Remediation completion must be supported by objective evidence.


The validation process may include:


- Document review;
- Configuration review;
- Interviews;
- Technical testing;
- Operational testing;
- Reassessment of the affected control.

The validation result must determine whether the original weakness has been effectively remediated.

14. Finding Closure Process

The finding closure process is:

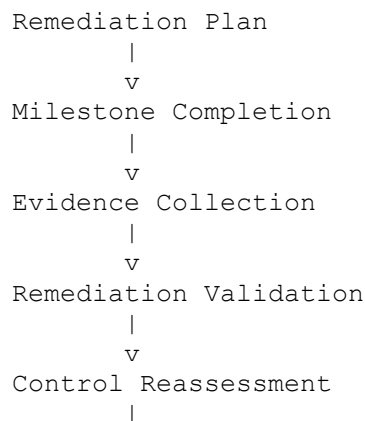



A finding may be closed only when the responsible authority determines that sufficient evidence demonstrates the weakness has been remediated.

15. Traceability Matrix

Source	Finding	POA&M	Remediation
SSP / AC-2	SAR-OCSP-001	POAM-001	Improve account lifecycle management
SSP / CM-2	SAR-OCSP-002	POAM-002	Complete configuration baselines
SSP / IR-3	SAR-OCSP-003	POAM-003	Conduct incident response exercise
SSP / SR-3	SAR-OCSP-004	POAM-004	Complete critical vendor reassessment

16. POA&M Review Frequency

The POA&M should be reviewed:

- At least monthly while active findings are being remediated;
- After significant changes to remediation plans;
- After reassessment activities;
- After significant security incidents;
- During authorization reviews;
- During continuous monitoring activities.

17. POA&M Conclusion

The Orion Citizen Services Platform POA&M documents four weaknesses identified during the July–August 2026 security assessment.

The weaknesses relate to:

1. Account lifecycle management;
2. Configuration baseline documentation;
3. Incident response exercise validation; and

4. Critical third-party vendor reassessment.

Each weakness has been assigned:

- A responsible organization;
- A remediation strategy;
- Defined milestones;
- A target completion date;
- Closure criteria; and
- A validation requirement.

The POA&M will remain active until remediation activities have been completed and the affected controls have been appropriately validated.

18. Document Status

Document: Plan of Action and Milestones

System: Orion Citizen Services Platform

System ID: OCSP-001

Version: 1.0

Status: Draft for Review

Source SAR: SAR-OCSP-2026-07

Active POA&M Items: 4

Next Activity: Remediation and Continuous Monitoring
